
PENSACOLA DOWNTOWN BRUCE BEACH DESIGN UPDATE



AGENDA

- Overview of the Project
 - Framework Plan
 - Updated Site Plan (Phase 1 & 2)
- What We Heard
- Project Status
 - Phase 1
 - Phase 2
- Next Steps
 - Project Schedule
- Questions

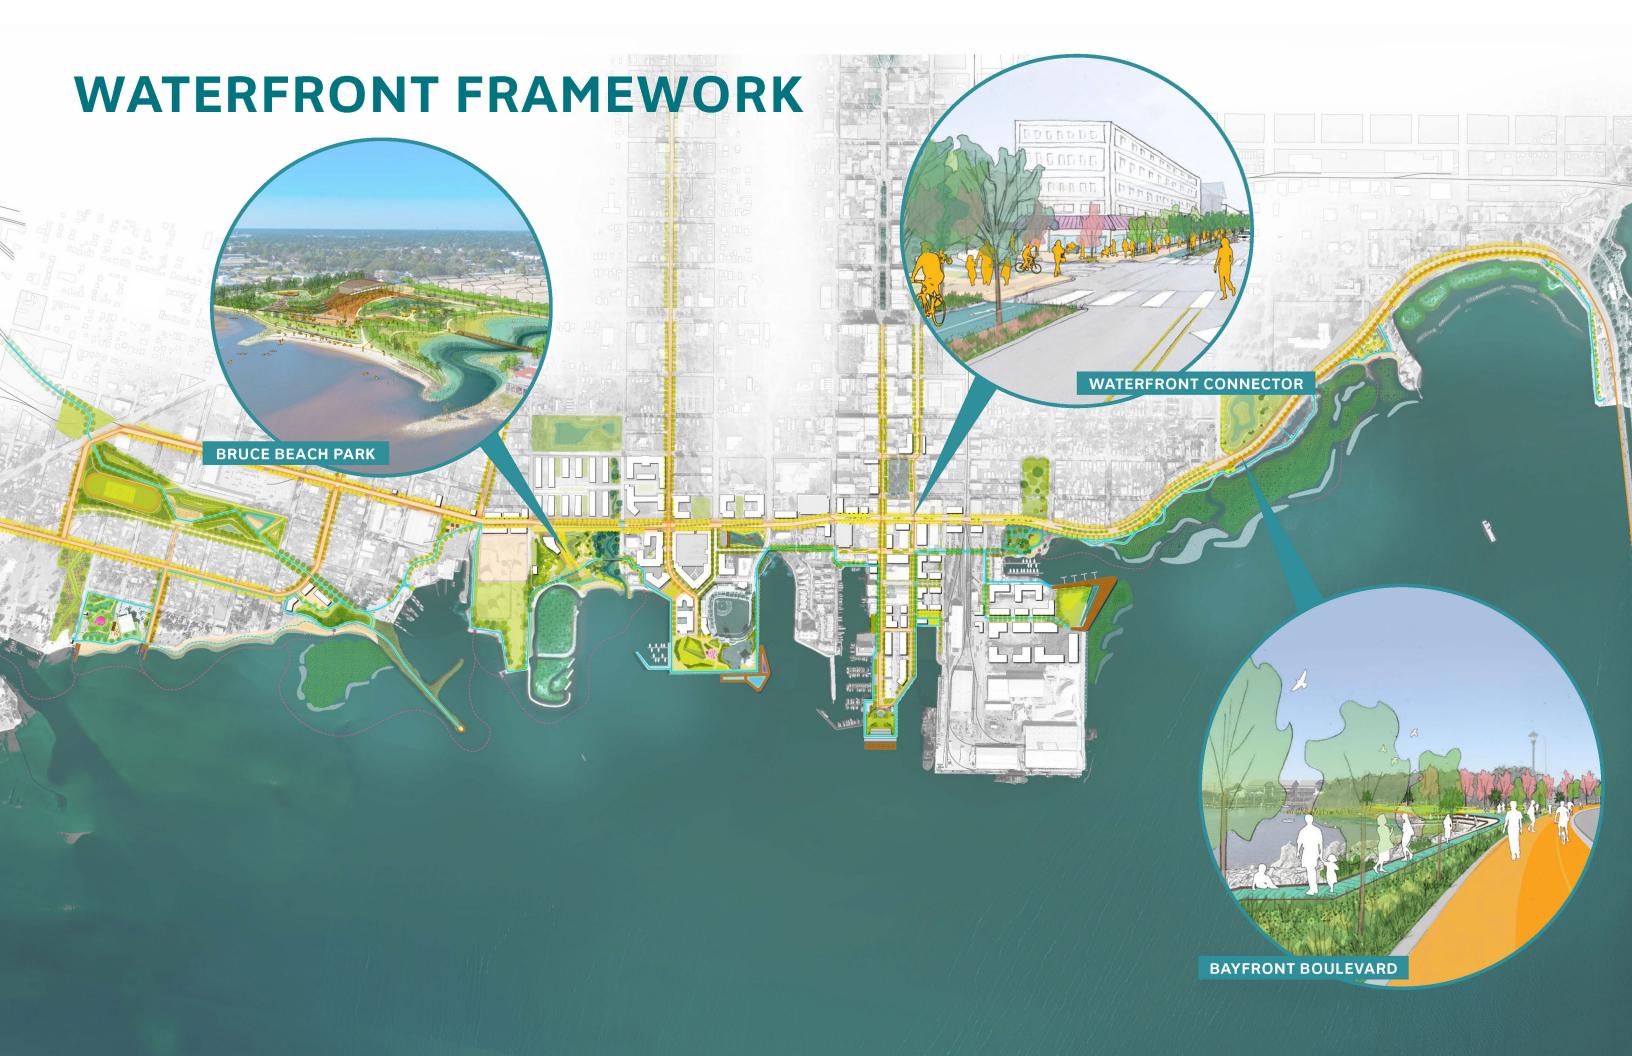

PROJECT GOALS









CREATEACULTURALAND EDUCATIONAL DESTINATION AT THE BAY'S EDGE





WHAT WE HEARD

WHAT WE HEARD

• Phase 1

• Reduce hardscaping wherever possible.

Phase 2 of the site plan leaves much of the site as softscape with many existing trees to remain and native planting.

Where are the restrooms?

At this time, there will be high quality temporary restroom trailer. At a later date, a permanent restroom will be constructed.

• Request for public parking closer to the Kayak Launch.

Due to the proximity of the waterfront, we have located the parking as close to the kayak launch as possible. In addition, this kayak stop is one of several on the existing kayak route, that many folks will not use as the primary point of access to the water.

Phase 2

Preserve existing trees.

We have performed a tree inventory, and have worked rigorously to maintain existing trees wherever possible. We have a diagram in the presentation that articulates this work.

• Request for low-light.

The updated plan utilizes minimum lighting to satisfy safety requirements. We understand the ecological concerns and have balanced this with safety needs.

Accessibility of pervious surfaces.

The updated plan allows access to the lawn area or sandy beach areas through grading and material surface changes.

PROJECT UPDATES

BRUCE BEACH - UPDATED PLAN



PHASE 1

PHASE 1 UPDATE - CONSTRUCTION PROGRESS

- Approximately 4 months remaining in construction
- Site grading nearly complete
- Forming of concrete features
- Site utilities & irrigation
- Pedestrian bridge has been set



HISTORY PLAZA - ALLEE



VIEW LOOKING SOUTH



SHADE STRUCTURE



VIEW LOOKING SOUTH



LEARNING GARDEN SEAT WALLS



VIEW LOOKING SOUTH



MARSH BRIDGE



VIEW LOOKING EAST



PATHWAY TO BEACH



VIEW LOOKING SOUTH



BEACHFRONT LOOKING NORTHWEST



SOUTH END OF ALLEE

FORMED PATHWAY



F) SCAPE

PHASE 2

PHASE 2 UPDATE - SITE DESIGN



ARRIVAL

- Entry Signage
- Parking & Drop-Off
- Clubbs St Rehab (in progress)
- Low-level Path Lighting

BLUFF APPROACH / OVERLOOK

- Boardwalk
- Preserved Oaks + Palm Grove
- Path to Overlook
- Mound Scramble
- Naturalized Berm & Terraces
- Low-level Path Lighting

KAYAK LAUNCH

- Kayak Storage
- Accessible Kayak Launch
- Seating Platform
- Restoration Area Trail

BEACHFRONT

- Sand Volleyball
- Picnic Area
- Seating at Preserved Palm Grove
- Restored Beach
- Low-level Path Lighting



PHASE 2 UPDATE - ARRIVAL










KAYAK LAUNCH

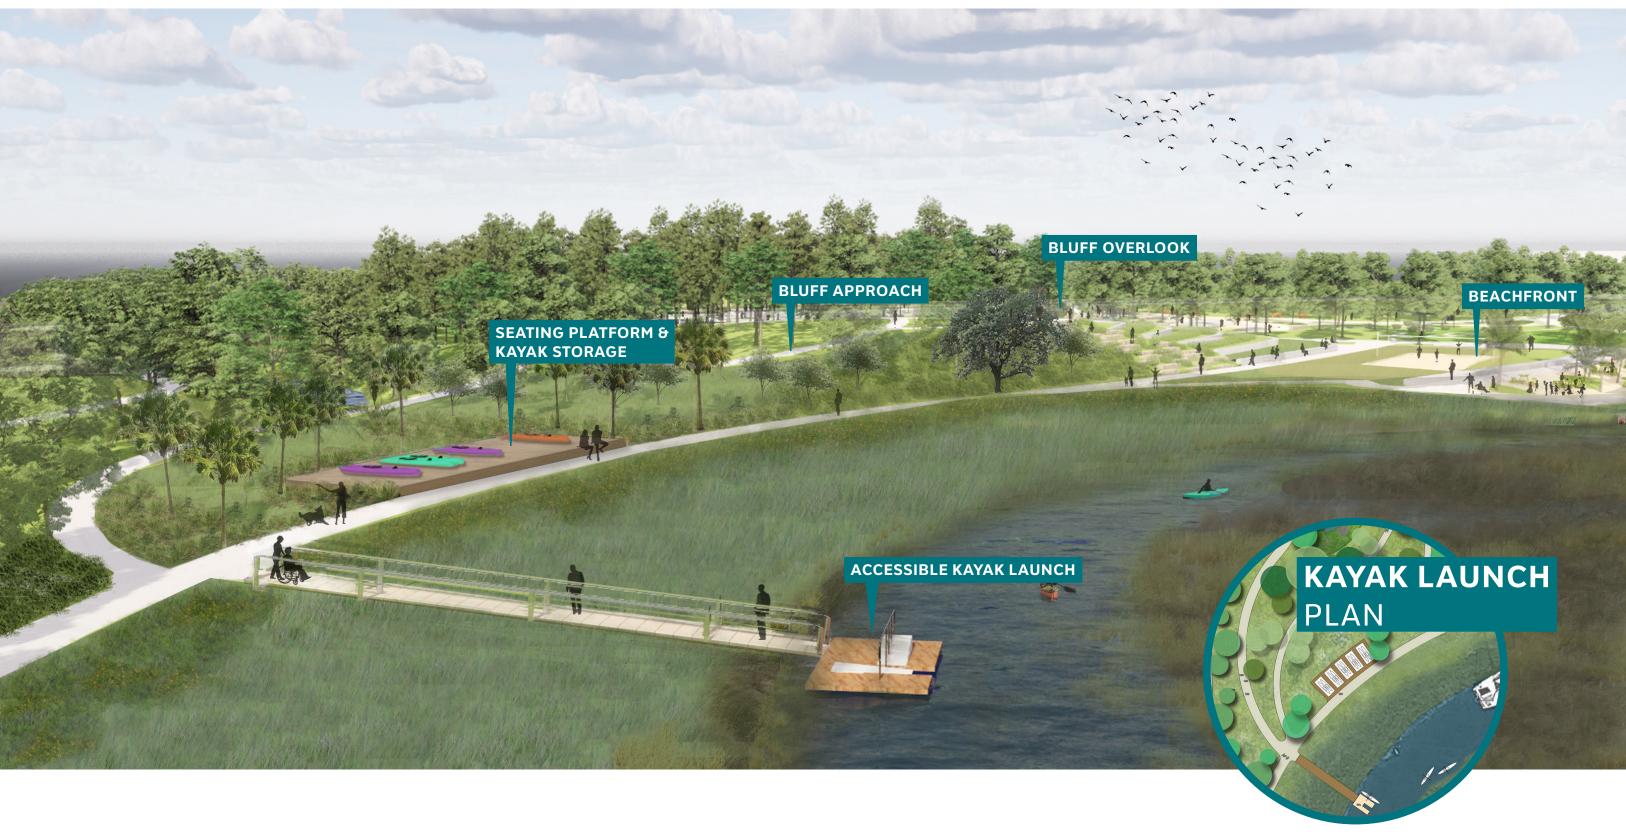




BLUFF OVERLOOK






TREE INVENTORY


TREE INVENTORY

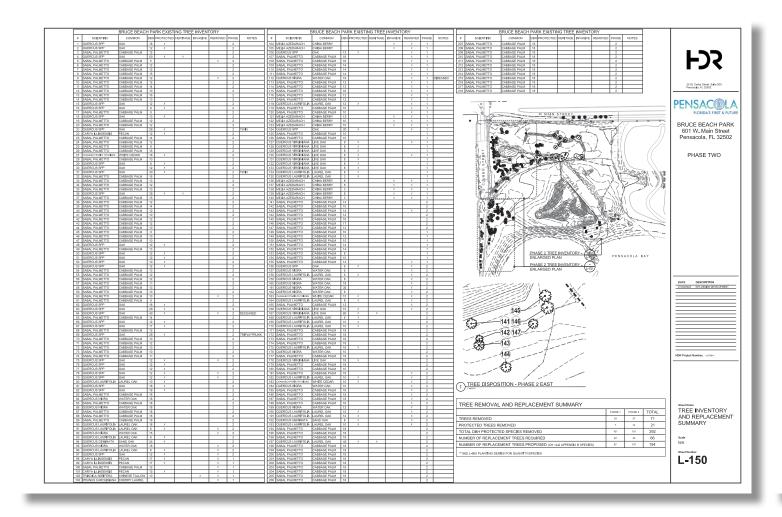

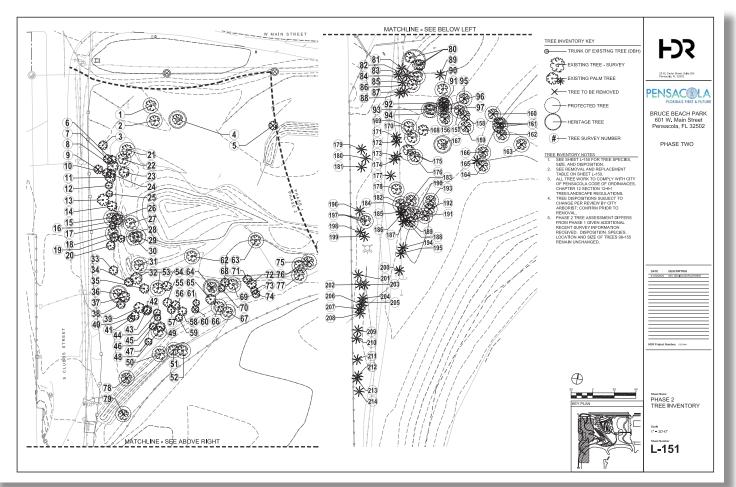



PROPOSED TREE CANOPY IMPROVEMENTS - 60% PLANS

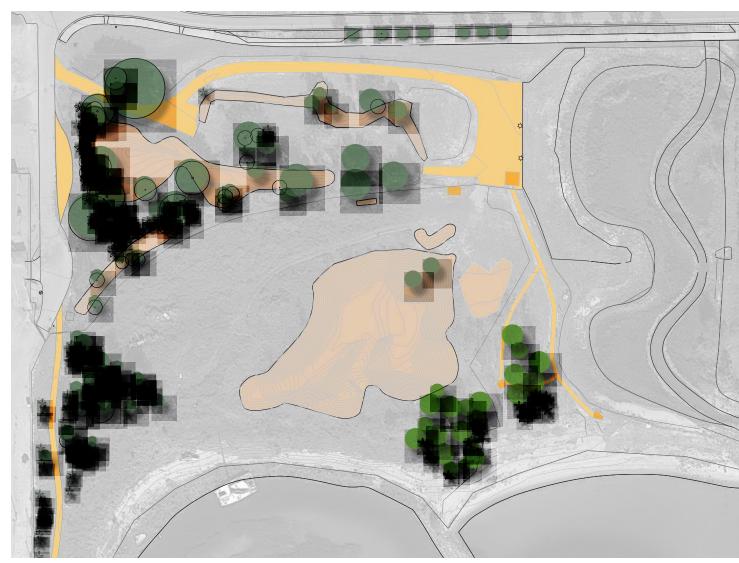

TREE CANOPY: EXISTING CONDITIONS



TREE CANOPY: FULL BUILD-OUT

TOTAL REMOVED DBH: 292"


REQUIRED NUMBER OF REPLACEMENT TREES: 66

PROPOSED TREES: 194



NEXT STEPS

PROJECT SCHEDULE

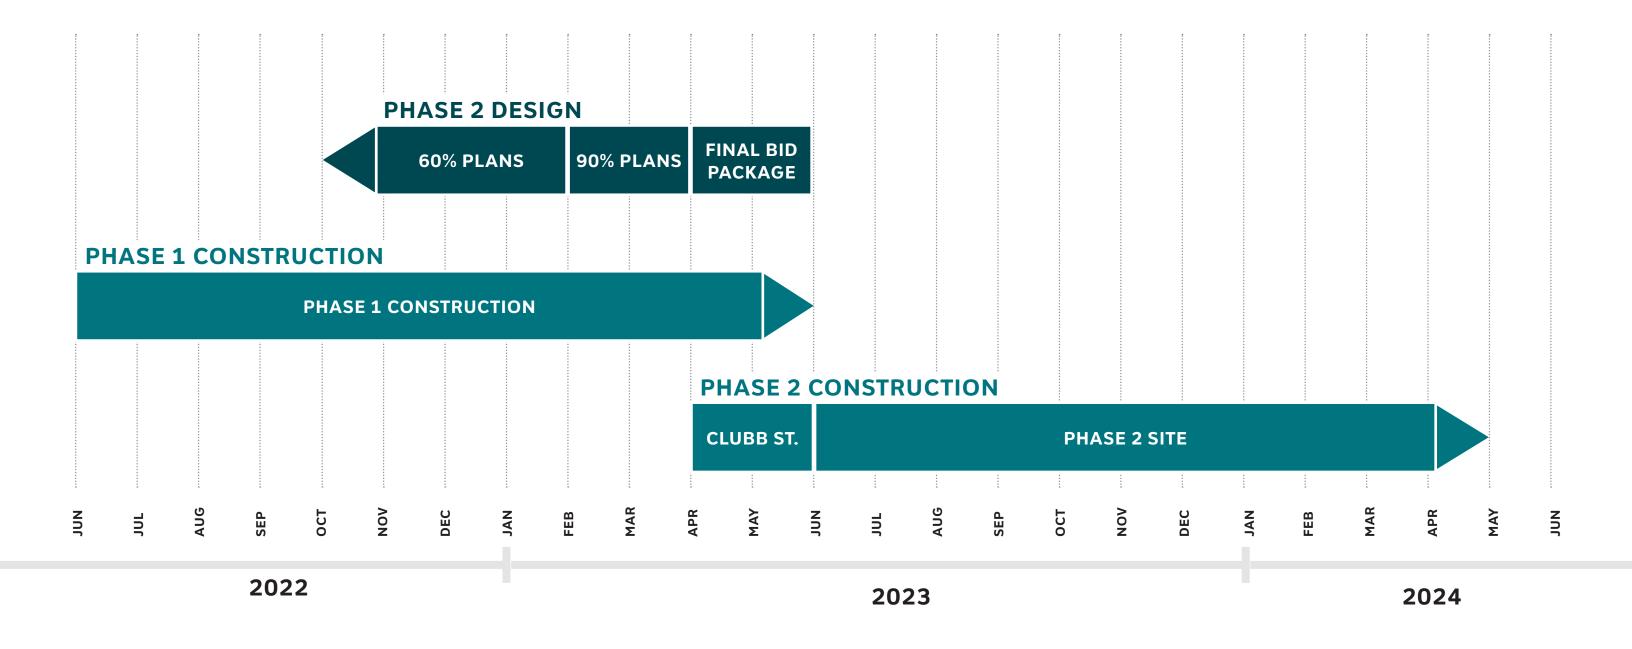



QUESTIONS?

THANK YOU!
